ID	Task Mode	Task Name	Duration	Start	Finish	Predecessors	Resource Names
1		**Shell Building Construction**	**180 days**	**Mon 7/25/22**	**Fri 3/31/23**		
2		Hollow Core Plank 1st Floor	5 days	Mon 7/25/22	Fri 7/29/22		
3		Edge Form 1st Floor	8 days	Wed 7/27/22	Fri 8/5/22		
4		Pour 1st Floor Topping	3 days	Mon 8/8/22	Wed 8/10/22		
5		Garage Slab Rough	9 days	Tue 8/9/22	Fri 8/19/22		
6		Masonry to 2nd Floor	12 days	Thu 8/11/22	Fri 8/26/22		
7		Garage SOB	5 days	Mon 8/22/22	Fri 8/26/22		
8		Beams & Columns	15 days	Mon 8/22/22	Fri 9/9/22		
9		Hollow Core Planks 2nd Floo	5 days	Mon 9/12/22	Fri 9/16/22		
10		Edge Form 2nd Floor	10 days	Thu 9/15/22	Wed 9/28/22		
11		Pour 2nd Floor Topping	3 days	Thu 9/29/22	Sat 10/1/22		
12		Interior Metal Framing 1st Fl	15 days	Mon 10/3/22	Fri 10/21/22		
13		MEP Rough In 1st Floor	15 days	Mon 10/17/22	Fri 11/4/22		
14		Masonry to 3rd Floor	10 days	Mon 10/3/22	Fri 10/14/22		
15		Beams & Columns	16 days	Wed 10/12/22	Wed 11/2/22		
16		Hollow Core Planks 3rd Floor	4 days	Thu 11/3/22	Tue 11/8/22		
17		Edge Form 3rd Floor	10 days	Mon 11/7/22	Fri 11/18/22		
18		Pour 3rd Floor Topping	3 days	Mon 11/21/22	Wed 11/23/22		
19		Interior Metal Framing 2nd F	15 days	Mon 11/28/22	Fri 12/16/22		
20		MEP Rough 2nd Floor	15 days	Mon 12/12/22	Fri 12/30/22		
21		Masonry to 4th Floor	10 days	Mon 11/28/22	Fri 12/9/22		
22		Beams & Columns	11 days	Wed 12/7/22	Wed 12/21/22		
23		Hollow Core Planks 4th Floor	5 days	Thu 12/22/22	Wed 12/28/22		
24		Edge Form 4th Floor	10 days	Mon 12/26/22	Fri 1/6/23		
25		Pour 4th Floor Topping	3 days	Mon 1/9/23	Wed 1/11/23		
26		Interior Metal Framing 3rd Fl	15 days	Mon 1/9/23	Fri 1/27/23		
27		MEP Rough 3rd Floor	15 days	Mon 1/23/23	Fri 2/10/23		
28		Masonry to Roof	10 days	Thu 1/12/23	Wed 1/25/23		
29		Windows	18 days	Wed 1/18/23	Fri 2/10/23		
30		Hollow Core Planks @ Roof	4 days	Thu 1/26/23	Tue 1/31/23		
31		Stucco	35 days	Mon 1/30/23	Fri 3/17/23		
32		Trash Chute	18 days	Wed 2/1/23	Fri 2/24/23		
33		Storefronts	6 days	Wed 2/1/23	Wed 2/8/23		
34		Drywall	33 days	Wed 2/1/23	Fri 3/17/23		
35		LWC Topping @ Roof	3 days	Wed 2/1/23	Fri 2/3/23		
36		Roofing	5 days	Mon 2/6/23	Fri 2/10/23		
37		Elevator	20 days	Mon 2/6/23	Fri 3/3/23		
38		Interior Metal Framing 4th Fl	15 days	Mon 2/6/23	Fri 2/24/23		

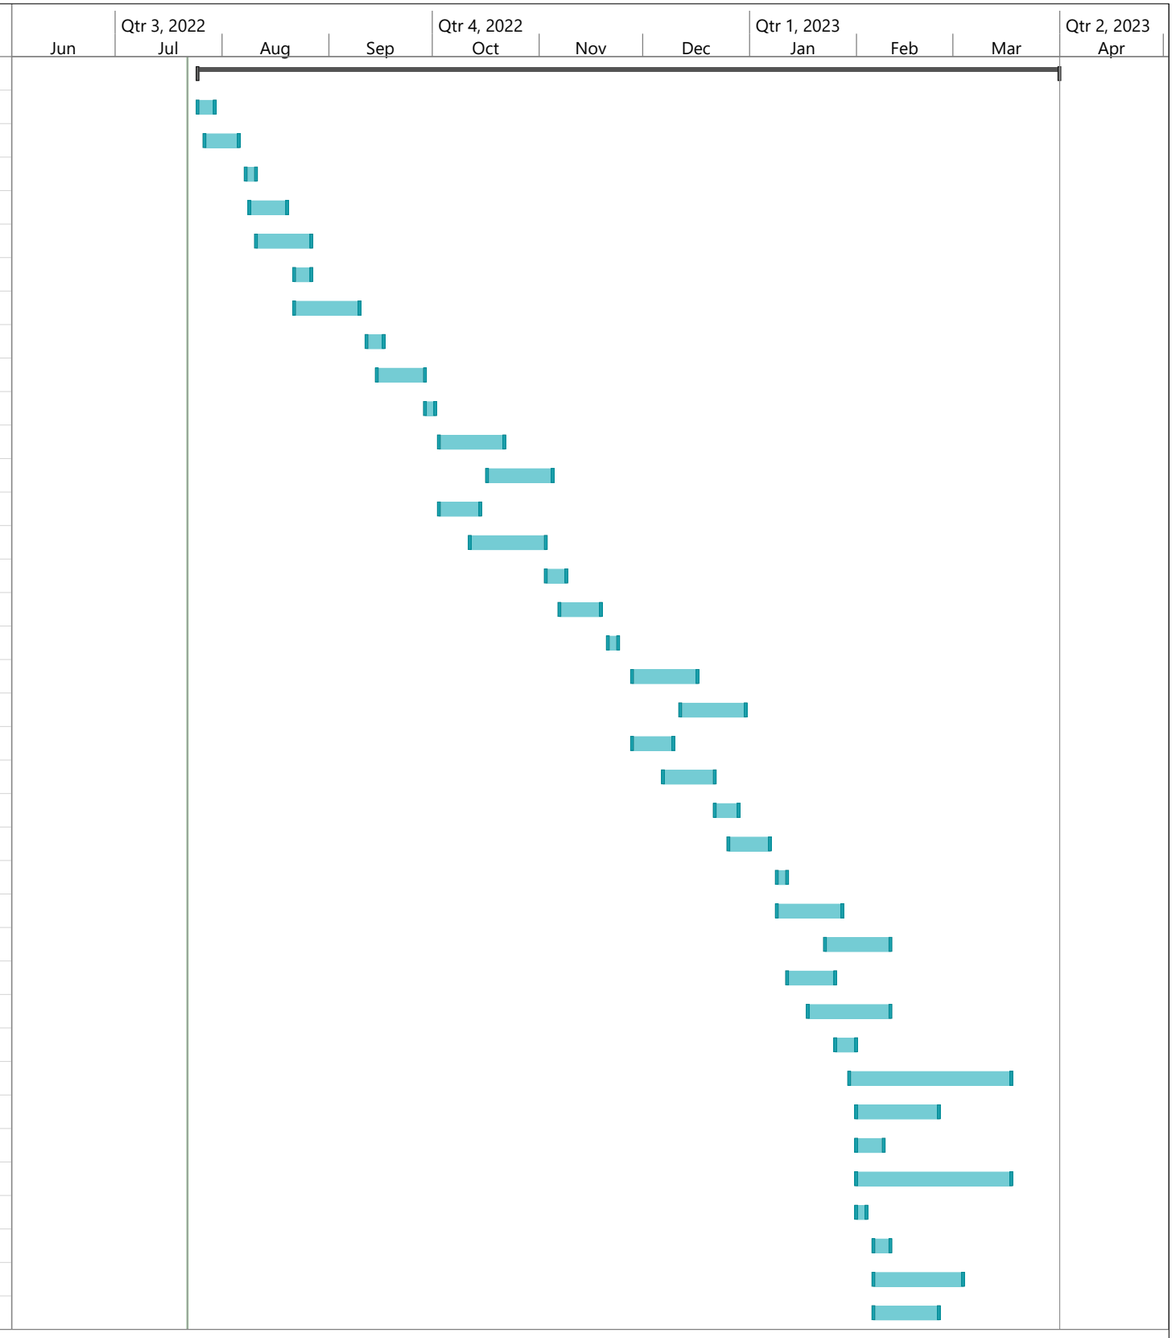

Project: 22003 Hidden Bay Con
Date: Fri 7/22/22

Task	Project Summary	Manual Task	Start-only	Deadline
Split	Inactive Task	Duration-only	Finish-only	Progress
Milestone	Inactive Milestone	Manual Summary Rollup	External Tasks	Manual Progress
Summary	Inactive Summary	Manual Summary	External Milestone	

ID	Task Mode	Task Name	Duration	Start	Finish	Predecessors	Resource Names
39		Interior Trims per plans	20 days	Mon 2/20/23	Fri 3/17/23		
40		MEP Rough In 4th Floor	15 days	Mon 2/20/23	Fri 3/10/23		
41		Interior Trims	23 days	Wed 3/1/23	Fri 3/31/23		
42		Decorative Aluminum Railings	18 days	Wed 3/1/23	Fri 3/24/23		
43		Balcony Screening	18 days	Wed 3/1/23	Fri 3/24/23		
44		Final Inspections	5 days	Mon 3/27/23	Fri 3/31/23		
45		Certificate of Occupancy/Shell	1 day	Fri 3/31/23	Fri 3/31/23		

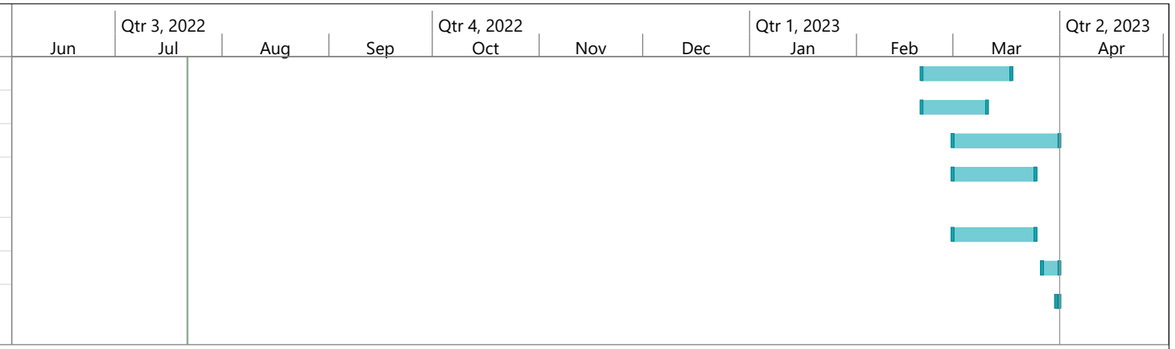

Project: 22003 Hidden Bay Con
Date: Fri 7/22/22

Task	Project Summary	Manual Task	Start-only	Deadline
Split	Inactive Task	Duration-only	Finish-only	Progress
Milestone	Inactive Milestone	Manual Summary Rollup	External Tasks	Manual Progress
Summary	Inactive Summary	Manual Summary	External Milestone	
